

**SAFETY IMPROVEMENTS ON NEW JERSEY AVENUE NW**  
**DC CONTRACT NO. DCKA-2018-C-0017**  
**FAP No.: CM-2017(042)**

---

**CONSTRUCTION MANAGER'S  
WEEKLY PROGRESS REPORT 25**

**10/27/2019 – 11/02/2019**

---

Project Website: [www.newjerseyaverehab.com](http://www.newjerseyaverehab.com)



10/29/2019- New block paver sidewalk on east side of NJ between K & L St. NW. (North view)

## 1. EXECUTIVE SUMMARY

### **Project Description:**

Work under this contract consists of safety/streetscape improvements along New Jersey Avenue, NW from N Street NW to H Street NW and the reconstruction New York Avenue, NW from First Street NW to 4th Street NW. The work includes but is not limited to the following items: Installation of new curb, gutter, and sidewalk; Installation of full depth pavement, Pavement resurfacing; Installation of utilities; Installation of flexible pavement; Installation of street light poles; Installation of traffic signals; Installation of signing and pavement markings; Installation of electrical duct bank; Relocation of over-height detection system; Installation of wireless vehicle detection system; Installation of landscape improvements; Installation of erosion and sediment control; Implementation of transportation management plan; Mobilization and demobilization, provision and maintenance of work and storage areas, Engineer's field facilities and performance of employee training; Removal and disposal of any material as a result of the activities listed above, unless stated otherwise in the contract drawings

This project is 83.15% Federally Funded and 16.85% District-Funded. DDOT selected Capitol Paving of DC, Inc. (CPDC) as the contractor and awarded the \$12,055,691.00 contract on January 9, 2019. DDOT issued notice to proceed with contract work to CPDC with work to begin on 05/13/2019 and a substantial completion date of 11/23/2020.

## 2. STATUS OF CONSTRUCTION / PROGRESS SUMMARY

The following were some of the work items performed during this reporting week period.

- Furnished and installed two (2) PCC foundation for Traffic Signal Pole at SW corner of K St. & New Jersey Ave. NW.
- Furnished and installed one (1) Standard Double Catch Basin at NY Ave. near Sta. 315+80
- Replaced 65 LF of water service pipe for H. No. 1232 NJ Ave. West side.
- Furnished and installed 36 LF of 4-4" Schedule 40 Rigid PVC Conduit (duct bank ) at M St. and NJ Ave. and NE Corner of NY Ave. and 4<sup>th</sup> St.
- Constructed 44.94 SY of Block sidewalk on PCC Base at SE corner of Pierce St. and NJ Ave.
- Installed seven (7) LF of 15" Basin Connect PCC pipe at NE corner of NY Ave. and NJ Ave. at approximate Sta. 315+50. (Between MH-J1 and CB-J2)
- Furnish and set 55.6 LF of 8"x12" granite straight curb at NW corner of NJ Ave and K St. NW.
- Performed 89.25 LF of 1' wide Brick gutter at SW corner of New Jersey and K St. NW.
- Constructed 76.17 SY of Brick sidewalk on Sand/Cement Bed at SW corner of New Jersey Ave. and K St. NW.
- Furnished and installed 38 LF of 4-4" PVC conduit at New Jersey Ave. and M St. NW.
- Removed two (2) abandoned Traffic Signal pole foundation at NW corner of NJ Ave. and K St. NW.
- Installed one (1) 4'x4'x4' Manhole (MH-3) at New Jersey Ave. between M St & Morgan St. NW.
- Furnished and installed 27 LF one 2" and one 4" PVC Encased electrical conduit between MH B & L2 (13LF) between MH B & TS2 (14LF).
- Furnished and install one 48"x48"x48" Manhole (MH-5) at East side of New Jersey Ave. NW between NY Ave. and M St. NW at approximate sta. No. 105+40.



### 3. PHOTOS OF WORK PERFORMED THIS PERIOD

*Picture No. 1*



10/29/2019- Brick sidewalk construction at West side of NJ Ave, South of K St. (North View)

*Picture No. 2*



10/29/2019- Compaction to the soil backfill for electric conduits buried at SW corner of NJ & K St. NW.



*Picture No. 3*



10/30/2019- Traffic Signal conduit installed at/near New Jersey Ave. & M St. NW. intersection.

*Picture No. 4*



10/30/2019-Relocate Traffic Signal on Temporary Base at NW corner of NJ Ave. & K St. NW. (West view)



Picture No. 5



10/30/2019-.Brick sidewalk construction at SW corner of New Jersey Ave & K St. NW (South view)


Picture No. 6



10/30/2019 – Preparing for water main shut down at NJ Ave. near N St. NW. (South view)



*Picture No. 7*

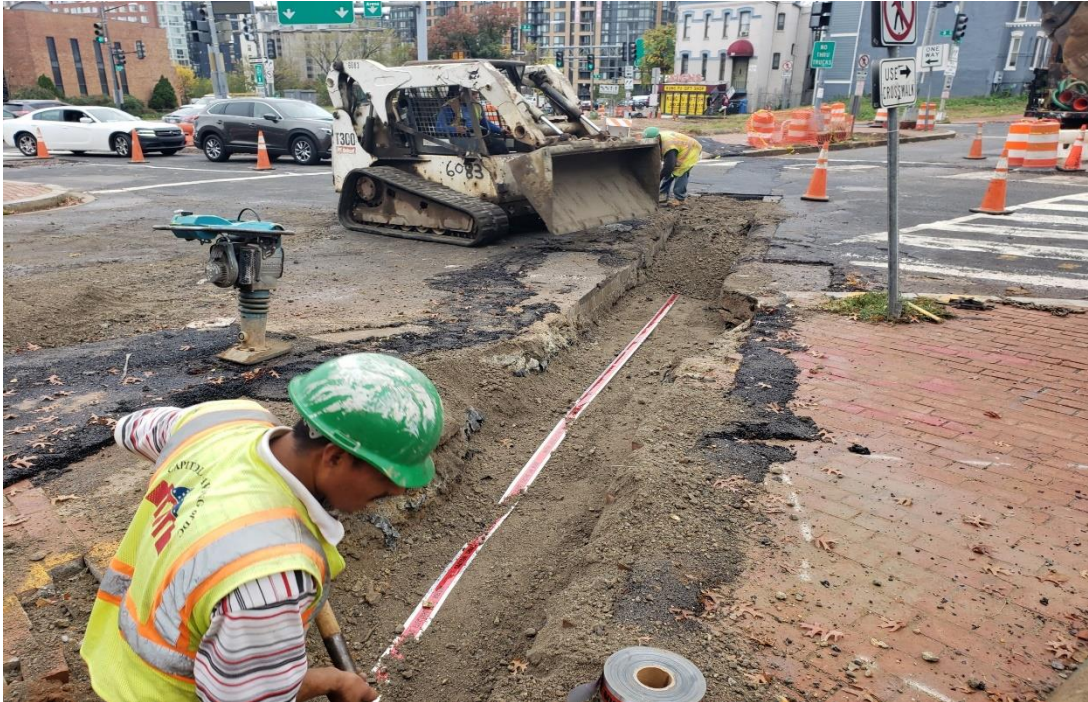

10/31/2019- Trench backfill for Traffic signal conduit installed at/near M St. & New Jersey Ave. NW.

*Picture No. 8*



11/01/2019- Working on streetlight at West side of NJ Ave NW near K St. NW. (North view)



Picture No. 9



11/01/2019- Excavation for streetlight manholes at NJ Ave. NW between NY & Morgan St. (North view)

Picture No. 10



11/01/2019- Excavation for streetlight conduit at NJ Ave. NW b/n Morgan and NY Ave. (Southwest View)
